McGraw Exterior Entrance Repair

155 Hyman Mall
Whitewater, WI

Listen. Plan. Deliver.

ID	Task Name	Duration	Start	Finish
1	**UW Whitewater - Exterior Entrance Repair**	**68 days**	**Sat 5/14/22**	**Sat 8/20/22**
2	Commencement Ceremony	1 day	Sat 5/14/22	Sat 5/14/22
3	**Site Demolition**	**10 days**	**Mon 5/16/22**	**Fri 5/27/22**
4	Install Erosion Control	1 day	Mon 5/16/22	Mon 5/16/22
5	Install Fencing	1 day	Mon 5/16/22	Mon 5/16/22
6	Sawcut Concrete for Demo	2 days	Tue 5/17/22	Wed 5/18/22
7	Remove railings	2 days	Tue 5/17/22	Wed 5/18/22
8	Remove Exterior Concrete	5 days	Wed 5/18/22	Tue 5/24/22
9	Remove Site Lighting	1 day	Thu 5/19/22	Thu 5/19/22
10	Bench Grades back @ Tunnel	1 day	Wed 5/25/22	Wed 5/25/22
11	Demo Tunnel section	2 days	Thu 5/26/22	Fri 5/27/22
12	**Building Enclosure**	**56 days**	**Mon 5/16/22**	**Wed 8/3/22**
13	Electrical & HVAC Demo and Rework in Tunnel	5 days	Mon 5/16/22	Fri 5/20/22
14	Infill Tunnel Openings - CMU	3 days	Mon 5/23/22	Thu 5/26/22
15	Excavate for Mech 33 & Vestibule Footings	1 day	Tue 5/31/22	Tue 5/31/22
16	Pour Mech & Vestibule Foundation Walls	4 days	Wed 6/1/22	Mon 6/6/22
17	Install Roof Blocking	2 days	Tue 6/7/22	Wed 6/8/22
18	Insulate and waterproof walls	3 days	Thu 6/9/22	Mon 6/13/22
19	Install HM Doors	2 days	Thu 6/9/22	Fri 6/10/22
20	Replace Membrane Roofing	5 days	Tue 6/14/22	Mon 6/20/22
21	Install Cement Board Siding	3 days	Tue 6/21/22	Thu 6/23/22
22	Install ships ladder	1 day	Fri 6/24/22	Fri 6/24/22
23	Electrical & HVAC Rough-In	10 days	Tue 6/21/22	Tue 7/5/22
24	Erect Temp barrier for Curtainwall	3 days	Thu 7/7/22	Mon 7/11/22
25	Replace Curtainwall	8 days	Tue 7/12/22	Thu 7/21/22
26	Start Wall & Soffit Framing	4 days	Mon 7/18/22	Thu 7/21/22
27	DEFS work	4 days	Fri 7/22/22	Wed 7/27/22
28	Interior Painting	4 days	Fri 7/22/22	Wed 7/27/22
29	ACT Patching	1 day	Thu 7/28/22	Thu 7/28/22
30	Flooring	3 days	Fri 7/29/22	Tue 8/2/22
31	Electrical Lighting	4 days	Fri 7/29/22	Wed 8/3/22
32	**New Site Pathways**	**41 days**	**Tue 5/31/22**	**Wed 7/27/22**
33	Excavate Switchback	1 day	Tue 5/31/22	Tue 5/31/22
34	Pour Switchback Foundations	5 days	Thu 6/2/22	Wed 6/8/22
35	Backfill Switchback	1 day	Thu 6/9/22	Thu 6/9/22
36	Pour Switchback Stairs	3 days	Fri 6/10/22	Tue 6/14/22
37	Excavate Monument Stair Footings	1 day	Tue 6/7/22	Tue 6/7/22
38	Pour Foundations for Monument Stair	7 days	Wed 6/8/22	Thu 6/16/22
39	Backfill Monument Stairs	1 day	Fri 6/17/22	Fri 6/17/22
40	Pour Monument stair sections	6 days	Mon 6/20/22	Mon 6/27/22
41	Install Monument Stair railings	3 days	Tue 6/28/22	Thu 6/30/22
42	Infill Bench Grading	3 days	Fri 6/17/22	Tue 6/21/22
43	Pour Upper stair sections	3 days	Wed 6/22/22	Fri 6/24/22
44	Pour McGraw SOG	5 days	Mon 6/27/22	Fri 7/1/22
45	Install Railings at upper stairs	3 days	Tue 7/5/22	Thu 7/7/22
46	Pour concrete paving	4 days	Tue 7/5/22	Fri 7/8/22
47	Install Site Lighting	7 days	Thu 6/30/22	Mon 7/11/22
48	Fine Grading Site	3 days	Mon 7/11/22	Wed 7/13/22
49	Landscaping	10 days	Thu 7/14/22	Wed 7/27/22
50	**Stair S3 Work**	**17 days**	**Mon 7/11/22**	**Tue 8/2/22**
51	Remove Rust from Steel	4 days	Mon 7/11/22	Thu 7/14/22
52	Remove VWC	2 days	Fri 7/15/22	Mon 7/18/22
53	Remove Flooring	1 day	Fri 7/15/22	Fri 7/15/22
54	Skim Coat Drywall	3 days	Tue 7/19/22	Thu 7/21/22
55	Paint walls	5 days	Fri 7/22/22	Thu 7/28/22
56	Install Flooring	3 days	Fri 7/29/22	Tue 8/2/22
57	Remove Exterior Concrete sidewalk	1 day	Mon 7/11/22	Mon 7/11/22
58	Pour new sidewalk	4 days	Tue 7/12/22	Fri 7/15/22
59	**Closeout**	**10 days**	**Mon 8/8/22**	**Sat 8/20/22**
60	Substantial Completion	1 day	Mon 8/8/22	Mon 8/8/22
61	Final Inspection	1 day	Mon 8/8/22	Mon 8/8/22
62	Punchlist	10 days	Mon 8/8/22	Sat 8/20/22
63	Owner Turnover	0 days	Sat 8/20/22	Sat 8/20/22

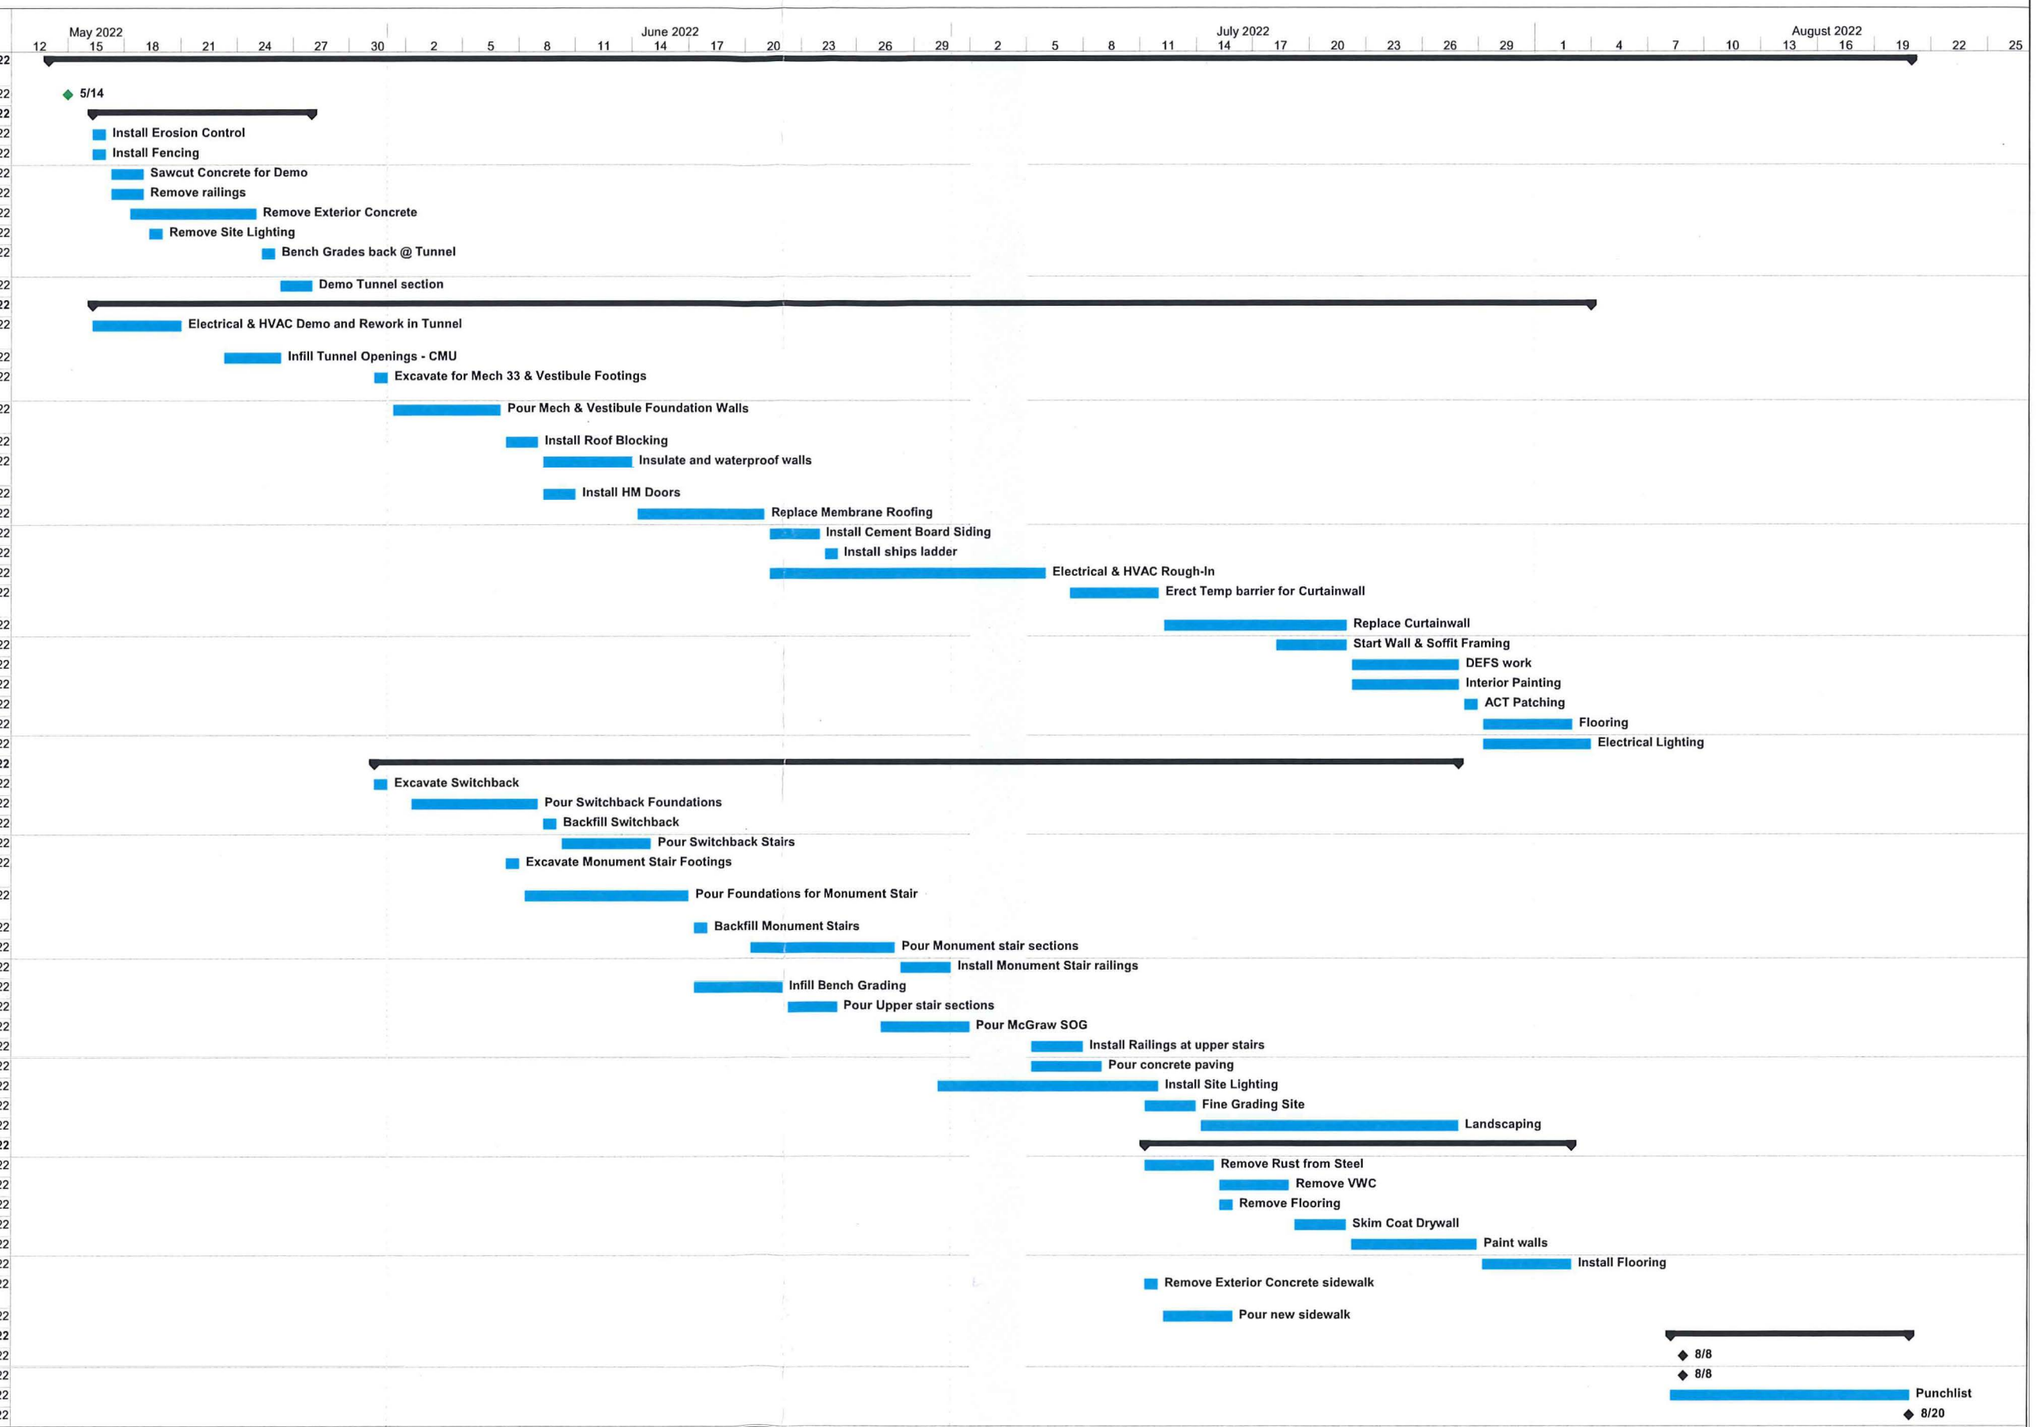

Project: Exterior Entrance Repair - McGraw Hall
Date: Mon 1/17/22

Task | Split | Milestone | Summary | Project Summary | Progress
